


| Act ID | Description | Orig Dur | Early Start | Early Finish | Total Float | WBS Code | 2018 | | | | | | 2019 | | | |
|--------------------------------|------------------------------|----------|-------------|--------------|-------------|----------|------------------------------|-----|-----|-----|-----|-----|------|-----|--|--|
| | | | | | | | JUL | AUG | SEP | OCT | NOV | DEC | JAN | FEB | | |
| ADMINISTRATIVE | | | | | | | | | | | | | | | | |
| | | 52d | 23MAY18 A | 03AUG18 | -9d | 3 | | | | | | | | | | |
| 1160 | CONTRACT AWARD | 1d | 23MAY18 A | 23MAY18 A | | 3 | CONTRACT AWARD | | | | | | | | | |
| 1170 | BOND DELIVERY | 9d | 28JUN18 A | 28JUN18 A | | 3 | BOND DELIVERY | | | | | | | | | |
| 1180 | MATERIAL SUBMITTALS | 7d | 02JUL18 A | 09JUL18 | 0 | 3 | MATERIAL SUBMITTALS | | | | | | | | | |
| 1186 | NOTICE TO PROCEED | 1d | 23JUL18 * | 03AUG18 | -9d | 3 | NOTICE TO PROCEED | | | | | | | | | |
| 1190 | | 3d | 02JUL18 | 02JUL18 | | 3 | | | | | | | | | | |
| CONSTRUCTION ACTIVITIES | | | | | | | | | | | | | | | | |
| | | 84d | 02JUL18 A | 26OCT18 | -5d | 4 | | | | | | | | | | |
| 1240 | MOBILIZE | 3d | 06AUG18 * | 08AUG18 | -9d | 4 | MOBILIZE | | | | | | | | | |
| 1250 | LAYDOWN AREA | 2d | 02JUL18 A | 10AUG18 | -9d | 4 | LAYDOWN AREA | | | | | | | | | |
| 1260 | 24 INCH RCP REPLACEMENT | 6d | 13AUG18 | 20AUG18 | -9d | 4 | 24 INCH RCP REPLACEMENT | | | | | | | | | |
| 1264 | 18 INCH RCP REPLACEMENT | 10d | 21AUG18 | 03SEP18 | -9d | 4 | 18 INCH RCP REPLACEMENT | | | | | | | | | |
| 1268 | 36 INCH RCP REPLACEMENT | 10d | 04SEP18 | 17SEP18 | -9d | 4 | 36 INCH RCP REPLACEMENT | | | | | | | | | |
| 1270 | TIDEFLEX VALVE INSTALLATIONS | 5d | 18SEP18 | 24SEP18 | -9d | 4 | TIDEFLEX VALVE INSTALLATIONS | | | | | | | | | |
| 1280 | CLEANING AND INSPECTION | 5d | 25SEP18 | 01OCT18 | -9d | 4 | CLEANING AND INSPECTION | | | | | | | | | |
| 1290 | 18X23 CURED IN PLACE LINER | 3d | 02OCT18 | 04OCT18 | -9d | 4 | 18X23 CURED IN PLACE LINER | | | | | | | | | |
| 1440 | 18 INCH CURED IN PLACE LINER | 5d | 05OCT18 | 11OCT18 | -9d | 4 | 18 INCH CURED IN PLACE LINER | | | | | | | | | |
| 1450 | 24 INCH CURED IN PLACE LINER | 5d | 12OCT18 | 18OCT18 | -9d | 4 | 24 INCH CURED IN PLACE LINER | | | | | | | | | |
| 1470 | 36 INCH CURED IN PLACE LINER | 5d | 19OCT18 | 25OCT18 | -9d | 4 | 36 INCH CURED IN PLACE LINER | | | | | | | | | |
| 1480 | POST VIDEO INSPECTION | 1d | 26OCT18 | 26OCT18 | -9d | 4 | POST VIDEO INSPECTION | | | | | | | | | |
| 1490 | | 1d | 02JUL18 | 02JUL18 | 78d | 4 | | | | | | | | | | |

| | |
|---------------------------|---------|
| Start date | 02JUL18 |
| Finish date | 01NOV18 |
| Data date | 02JUL18 |
| Run date | 02JUL18 |
| Page number | 1A |
| © Primavera Systems, Inc. | |

TRIAD ENGINEERING & CONTRACTING, INC
Seabrook Island Relining and Storm

- █ Early bar
- █ Early bar
- █ Progress bar
- █ Critical bar
- █ Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

| Act ID | Description | Orig Dur | Early Start | Early Finish | Total Float | WBS Code | 2018 | | | | | | 2019 | | | |
|------------------|------------------------------|----------|-------------|--------------|-------------|----------|------|-----|-----|-----|-----|-----|------|-----|--|--|
| | | | | | | | JUL | AUG | SEP | OCT | NOV | DEC | JAN | FEB | | |
| CLOSE OUT | | | | | | | | | | | | | | | | |
| | | 4d | 29OCT18 | 01NOV18 | -9d | 5 | | | | | | | | | | |
| 1080 | PROJECT WALK THRU | 1d | 29OCT18 | 29OCT18 | -9d | 5 | | | | | | | | | | |
| 1090 | PUNCH LIST | 1d | 30OCT18 | 30OCT18 | -9d | 5 | | | | | | | | | | |
| 1100 | SUBSTANTIAL COMPLETION FORMS | 1d | 31OCT18 | 31OCT18 | -9d | 5 | | | | | | | | | | |
| 1110 | VENDOR CERTIFICATES | 1d | 01NOV18 | 01NOV18 | -9d | 5 | | | | | | | | | | |

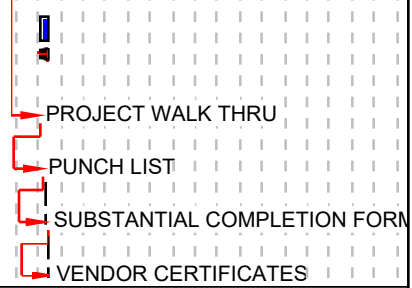

| | |
|---------------------------|---------|
| Start date | 02JUL18 |
| Finish date | 01NOV18 |
| Data date | 02JUL18 |
| Run date | 02JUL18 |
| Page number | 2A |
| © Primavera Systems, Inc. | |

TRIAD ENGINEERING & CONTRACTING, INC
Seabrook Island Relining and Storm

- █ Early bar
- █ Early bar
- █ Progress bar
- █ Critical bar
- █ Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point
